Presentation to MT Senate Energy Committee January 29, 2009

Bob Williams, P. Eng. MBA
Vice President Regulatory
Montana Alberta Tie Ltd.

MONTANA ALBERTA TIE LTD



Senate Energy & Telecomm.
Exhibit No. 3
Date 1-29-2009
Bill No.

Our Presentation

- Project Overview
- Approved Route
- Project Status
- Approval Time Frames & Uncertainty

MONTANA ALBERTA TIE LTD

Project Overview

- 230 kV – 300 MW
- 214 miles long, 130 miles in MT
- Merchant Transmission – Only Users Pay
- Customers are wind developers
- 600 MW of wind energy - $US 1 Billion

Route Map

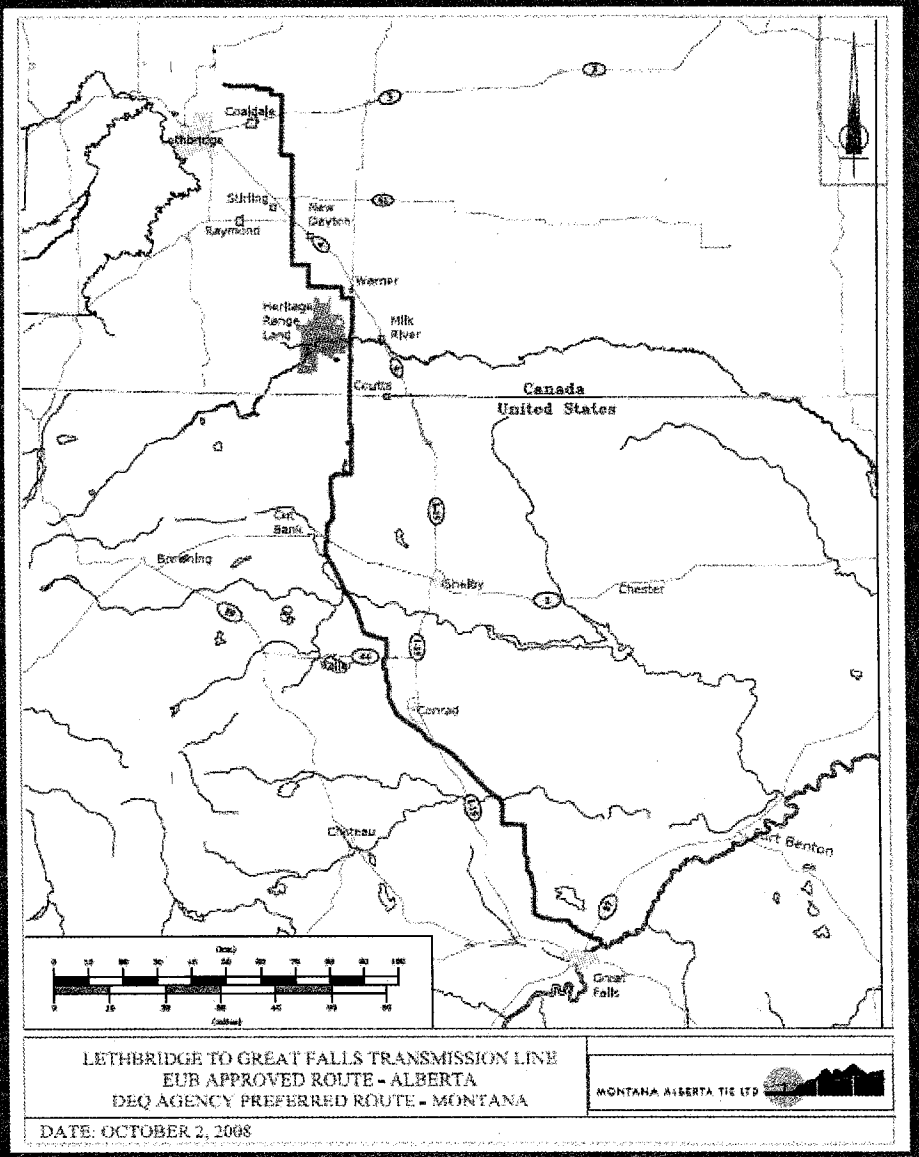
Coaldale
Lethbridge
Stirling
Raymond
Magrath
Warner
Heritage Range Land
Milk River
Coutts
Canada
United States
Cut Bank
Browning
Shelby
Chester
Conrad
Chinook
Fort Benton
Great Falls
LETHBRIDGE TO GREAT FALLS TRANSMISSION LINE
EUB APPROVED ROUTE - ALBERTA
DEQ AGENCY PREFERRED ROUTE - MONTANA
MONTANA ALBERTA TIE LTD
DATE: OCTOBER 2, 2008

Project Status

- Last of major permits received November, 2008
- Active negotiations with AB landowners since spring 2008
- Negotiations with MT landowners will commence soon
- Most of project financing in place, working on remaining details

MONTANA ALBERTA TIE LTD

Project Status

- AB Court of Appeal hearing – Jan 23
  - Court to reserve decision
  - Two issues – legal interpretation
- MT BER Hearing Order – Dec 23
  - Hearing dates: May 18 – 22
  - Schedule also set for steps up to hearing

MONTANA ALBERTA TIE LTD

Approval Time Frames & Uncertainty

- FERC – typically 3 to 9 months
- WECC – 24 months
- DEQ – 34 months (estimate: 9 mo)
- DOE – 37 months (estimate: 18 mo)
- AEUB – 24 months (estimate: 6 mo)
- NEB – 16 months (estimate: 6 mo)

MONTANA ALBERTA TIE LTD



Contact and Further Information

- Bob Williams
- Phone: (403) 264-4465
- Email: bob.williams@matl.ca
- MATL website: www.matl.ca
- Tonbridge website: www.tonbridgepower.com

MONTANA ALBERTA TIE LTD
